Réseaux

Read-only view, generated on 09 Oct 2025

Instagant
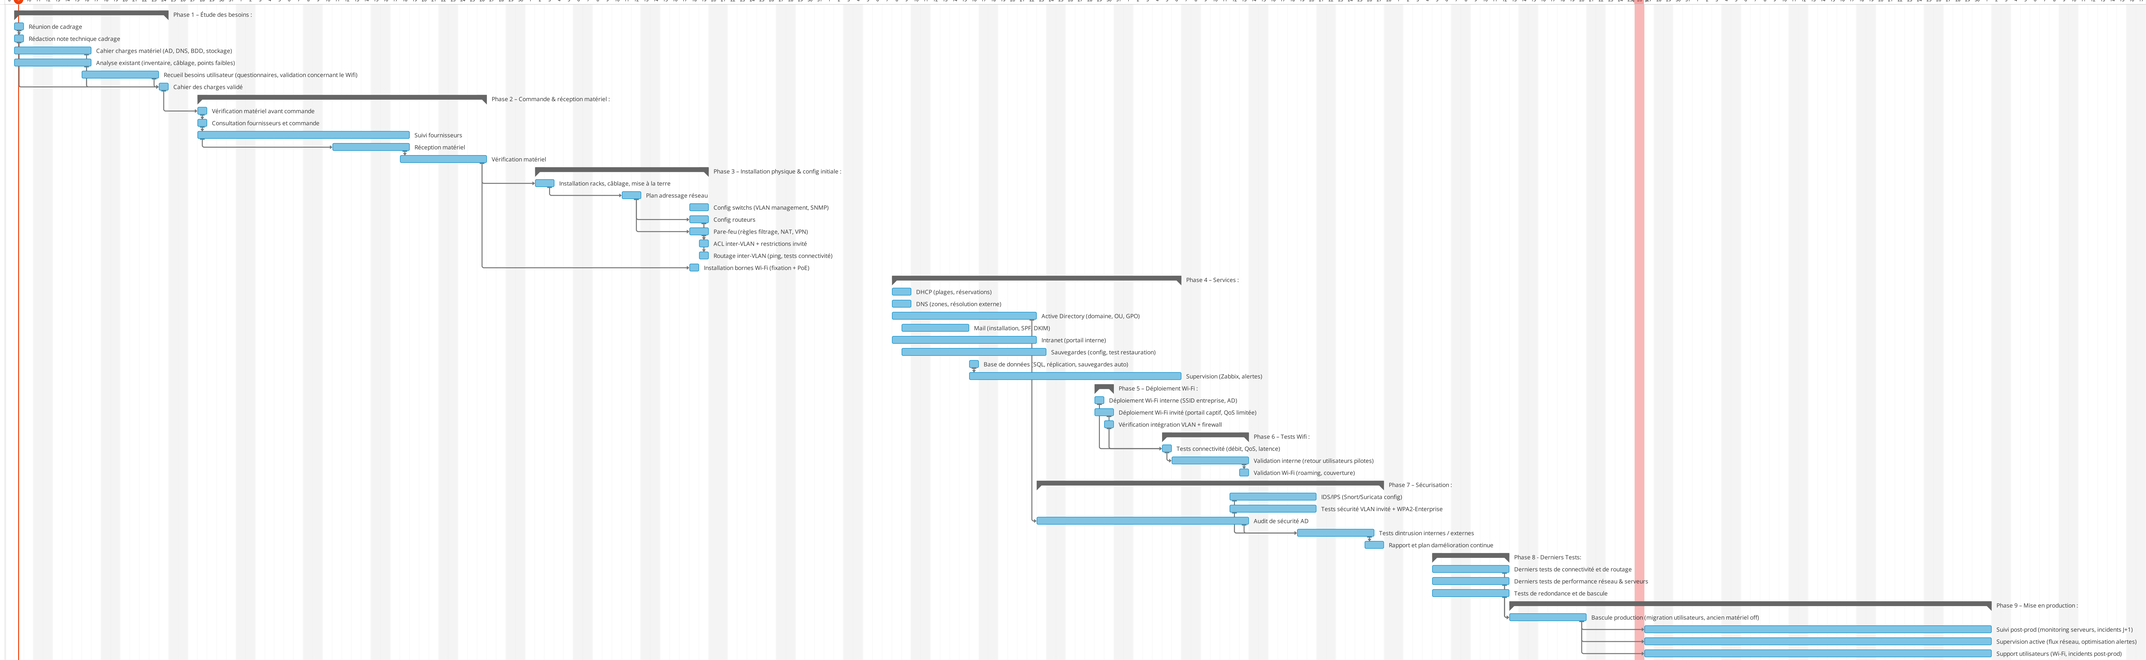
	ACTIVITIES	ASSIGNEE	EH	START	DUE	STATUS	%
	Phase 1 – Étude des besoins :		-	**09/Oct**	**24/Oct**		**0%**
1	Réunion de cadrage	Fr, Lo, Ma, We	-	09/Oct	09/Oct	Not started	0%
2	Rédaction note technique cadrage	Fr, Lo, Ma, We	-	09/Oct	09/Oct	Not started	0%
3	Cahier charges matériel (AD, DNS, BDD, stockage)	Fr, Lo, Ma, We	-	09/Oct	16/Oct	Not started	0%
4	Analyse existant (inventaire, câblage, points faibles)	Ligthan	-	09/Oct	16/Oct	Not started	0%
5	Recueil besoins utilisateur (questionnaires, validation concernant l...	Lo, Fr, Ma, We	-	16/Oct	23/Oct	Not started	0%
6	Cahier des charges validé	Fr, Lo, Ma, We	-	24/Oct	24/Oct	Not started	0%
	Phase 2 – Commande & réception matériel :		-	**28/Oct**	**26/Nov**		**0%**
8	Vérification matériel avant commande	Maxime	-	28/Oct	28/Oct	Not started	0%
9	Consultation fournisseurs et commande	Francesco	-	28/Oct	28/Oct	Not started	0%
10	Suivi fournisseurs	Wael	-	28/Oct	18/Nov	Not started	0%
11	Réception matériel	Wael	-	11/Nov	18/Nov	Not started	0%
12	Vérification matériel	We, Ma, Fr, Lo	-	18/Nov	26/Nov	Not started	0%
	Phase 3 – Installation physique & config initiale :		-	**02/Dec**	**19/Dec**		**0%**
14	Installation racks, câblage, mise à la terre	Fr, Lo, Ma, We	-	02/Dec	03/Dec	Not started	0%
15	Plan adressage réseau	Fr, Lo, Ma, We	-	11/Dec	12/Dec	Not started	0%
16	Config switchs (VLAN management, SNMP)	Lo, Ma	-	18/Dec	19/Dec	Not started	0%
17	Config routeurs	Fr, Lo	-	18/Dec	19/Dec	Not started	0%
18	Pare-feu (règles filtrage, NAT, VPN)	Ma, Lo	-	18/Dec	19/Dec	Not started	0%
19	ACL inter-VLAN + restrictions invité	Fr, Ma, Lo	-	19/Dec	19/Dec	Not started	0%
20	Routage inter-VLAN (ping, tests connectivité)	Lo, Fr	-	19/Dec	19/Dec	Not started	0%
21	Installation bornes Wi-Fi (fixation + PoE)	Wael	-	18/Dec	18/Dec	Not started	0%
	Phase 4 – Services :		-	**08/Jan**	**06/Feb**		**0%**
23	DHCP (plages, réservations)	Francesco	-	08/Jan	09/Jan	Not started	0%
24	DNS (zones, résolution externe)	Francesco	-	08/Jan	09/Jan	Not started	0%
25	Active Directory (domaine, OU, GPO)	Maxime	-	08/Jan	22/Jan	Not started	0%
26	Mail (installation, SPF, DKIM)	Francesco	-	09/Jan	15/Jan	Not started	0%
27	Intranet (portail interne)	Wael	-	08/Jan	22/Jan	Not started	0%
28	Sauvegardes (config, test restauration)	Ligthan	-	09/Jan	23/Jan	Not started	0%
29	Base de données (SQL, réplication, sauvegardes auto)	Fr, Lo	-	16/Jan	16/Jan	Not started	0%
30	Supervision (Zabbix, alertes)	Fr, Lo	-	16/Jan	06/Feb	Not started	0%
	Phase 5 – Déploiement Wi-Fi :		-	**29/Jan**	**30/Jan**		**0%**
32	Déploiement Wi-Fi interne (SSID entreprise, AD)	Wael	-	29/Jan	29/Jan	Not started	0%
33	Déploiement Wi-Fi invité (portail captif, QoS limitée)	Wael	-	29/Jan	30/Jan	Not started	0%
34	Vérification intégration VLAN + firewall	Wael	-	30/Jan	30/Jan	Not started	0%
	Phase 6 – Tests Wifi :		-	**05/Feb**	**13/Feb**		**0%**
36	Tests connectivité (débit, QoS, latence)	Wael	-	05/Feb	05/Feb	Not started	0%
37	Validation interne (retour utilisateurs pilotes)	Wael	-	06/Feb	13/Feb	Not started	0%
38	Validation Wi-Fi (roaming, couverture)	Wael	-	13/Feb	13/Feb	Not started	0%
	Phase 7 – Sécurisation :		-	**23/Jan**	**27/Feb**		**0%**
40	IDS/IPS (Snort/Suricata config)	Ligthan	-	12/Feb	20/Feb	Not started	0%
41	Tests sécurité VLAN invité + WPA2-Enterprise	Francesco	-	12/Feb	20/Feb	Not started	0%
42	Audit de sécurité AD	Maxime	-	23/Jan	13/Feb	Not started	0%
43	Tests dintrusion internes / externes	We, Fr, Lo, Ma	-	19/Feb	26/Feb	Not started	0%
44	Rapport et plan damélioration continue	Fr, Lo, Ma, We	-	26/Feb	27/Feb	Not started	0%
	Phase 8 - Derniers Tests:		-	**05/Mar**	**12/Mar**		**0%**
46	Derniers tests de connectivité et de routage	Fr, Lo	-	05/Mar	12/Mar	Not started	0%
47	Derniers tests de performance réseau & serveurs	We, Lo	-	05/Mar	12/Mar	Not started	0%
48	Tests de redondance et de bascule	Ma, Lo	-	05/Mar	12/Mar	Not started	0%
	Phase 9 – Mise en production :		-	**13/Mar**	**01/May**		**0%**
50	Bascule production (migration utilisateurs, ancien matériel off)	Lo, Fr, Ma, We	-	13/Mar	20/Mar	Not started	0%
51	Suivi post-prod (monitoring serveurs, incidents J+1)	Fr, Lo, Ma, We	-	27/Mar	01/May	Not started	0%
52	Supervision active (flux réseau, optimisation alertes)	Fr, Lo, Ma, We	-	27/Mar	01/May	Not started	0%
53	Support utilisateurs (Wi-Fi, incidents post-prod)	Fr, Ma, Lo, We	-	27/Mar	01/May	Not started	0%
